



References

- Angus, Robert B., Gundersen, Norman A. and Cullinane, Thomas P. (2000) Planning, Performing, and Controlling Projects. Prentice Hall. Upper Saddle River.
- Bent, James A. and Humphreys, Kenneth K. (1996) Effective Project Management through Applied Cost and Schedule Control. Marcel Dekker, Inc. New York.
- Burke, Rory (1999) Project Management: Planning and Control Techniques. John Wiley & Sons Ltd. Chichester.
- Buttrick, Robert (2000) The Project Workout: A toolkit for reaping the rewards from all your business projects. Financial Times. Prentice Hall. London.
- Dingle, John. (1997) Project Management: Orientation for Decision Makers. Arnold. London.
- Duncan, William R. (1996) A Guide to the Project Management Body of Knowledge. Project Management Institute Standards Committee. Upper Darby, PA.
- Field, Mike and Keller, Laurie. (1998) Project Management. International Thompson Business Press. London.
- Gido, Jack (1999) Successful Project Management. South-Western College Publication. Ohio.
- Gray, Clifford and Larson, Erik (2002) Project Management: The Complete Guide for Every Manager. McGraw-Hill. New York.
- Harrison, F. L. (1992) Advanced Project Management: A Structured Approach. Gower. Hants.
- Howes, Norman R. (2001) Modern Project Management. American Management Association. New York.
- Kerzner, Harold (1982) Project Management for Executives. Van Nostrand Reinhold. New York.
- Kerzner, Harold (1998) Project Management: A Systems Approach to Planning, Scheduling, and Controlling. John Wiley & Sons, Inc. New York.

- Knutson, Joan. (2001) Project Management for Business Professionals: A Comprehensive Guide. John Wiley. New York.
- Levine, Harvey A. (2002) Practical Project Management, Tips, Tactics, and Tools. John Wiley & Sons, Inc. New York.
- Lewis, James P. (2000) The Project Manager's Desk Reference: A Comprehensive Guide to Project Planning, Scheduling, Evaluation, and Systems. McGraw-Hill. Boston, MA.
- Lewis, James P. (2001) Project Planning Scheduling & Control. McGraw-Hill. New York.
- Lientz, Bennet P. and Rea, Kathryn P. (1998) Project Management for the 21st Century. Academic Press. San Diego.
- Martin, Paula and Tate, Karen (2001) Getting Started in Project Management. John Wiley & Sons, Inc. New York.
- Maylor, Harvey (1999) Project Management. Financial Times Management. London.
- Meredith, Jack R. and Mantel, Samuel J. Jr. (2000) Project Management A Managerial Approach. John Wiley & Sons. New York.
- Newbold, Robert C. (1998) Project Management in the Fast Lane: Applying the Theory to Constraints. St. Lucia Press. Florida.
- Project Management Institute Standards Committee (1996) A Guide to the Project Management Body of Knowledge. Upper Darby, PA: Project Management Institute.
- Roman, Daniel D. (1986) Managing Projects A Systems Approach. Elsevier Science Publishing. New York.
- Samaras, Thomas T. (1979) Computerized Project Management Techniques for Manufacturing and Construction Industries. Prentice Hall. New Jersey.

Seah, Seow Buay, Teh, Tuan Ann, and Ong Chin Tiong (1997) Project Management: How to Plan, Control and Manage Project. Prentice Hall. Simnn and Schuster. Singapore.

Appendices

Appendix A
Overall Project Schedule

Microsoft Project - Master

File Edit View Insert Format Tools Project Collaborate Window Help

Tasks Resources Track Report Next Steps and Related Activities

Mechanical and electrical installation project

WBS	Task Name	Duration	Oct '03	05 Jan '04	29 Mar '04	21 Jun '04	13 Sep '04	06 Dec '04	28 Feb	
			W	S	T	M	F	T	S	
1	Mechanical and electrical installa	261 days	[Gantt bar]							
2	1.1 Feasibility	9 days	[Gantt bar]							
3	1.1.1 Project formulation	2 days	[Gantt bar]							
4	1.1.2 Feasibility studies	4 days	[Gantt bar]							
5	1.1.3 Strategy design and approval	3 days	[Gantt bar]							
6	1.1.4 Feasibility ended	0 days	[Gantt bar]							
7	1.2 Planning and design	30 days	[Gantt bar]							
8	1.2.1 Base design	15 days	[Gantt bar]							
9	1.2.2 Cost and schedule	30 days	[Gantt bar]							
10	1.2.3 Contract terms and conditions	7 days	[Gantt bar]							
11	1.2.4 Detailed planning	30 days	[Gantt bar]							
12	1.2.5 Planning and design ended	0 days	[Gantt bar]							
13	1.3 Production	165 days	[Gantt bar]							
14	1.3.1 Material purchase	165 days	[Gantt bar]							
15	1.3.2 Engineering	84 days	[Gantt bar]							
16	1.3.3 Installation	165 days	[Gantt bar]							
17	1.3.4 Testing	165 days	[Gantt bar]							
18	1.3.5 Production ended	0 days	[Gantt bar]							
19	1.4 Turnover and startup	60 days	[Gantt bar]							
20	1.4.1 Commissioning	60 days	[Gantt bar]							
21	1.4.2 Maintenance	60 days	[Gantt bar]							

Ready


start


Microsoft Project - M...

12:53

Appendix B

Installation Schedule

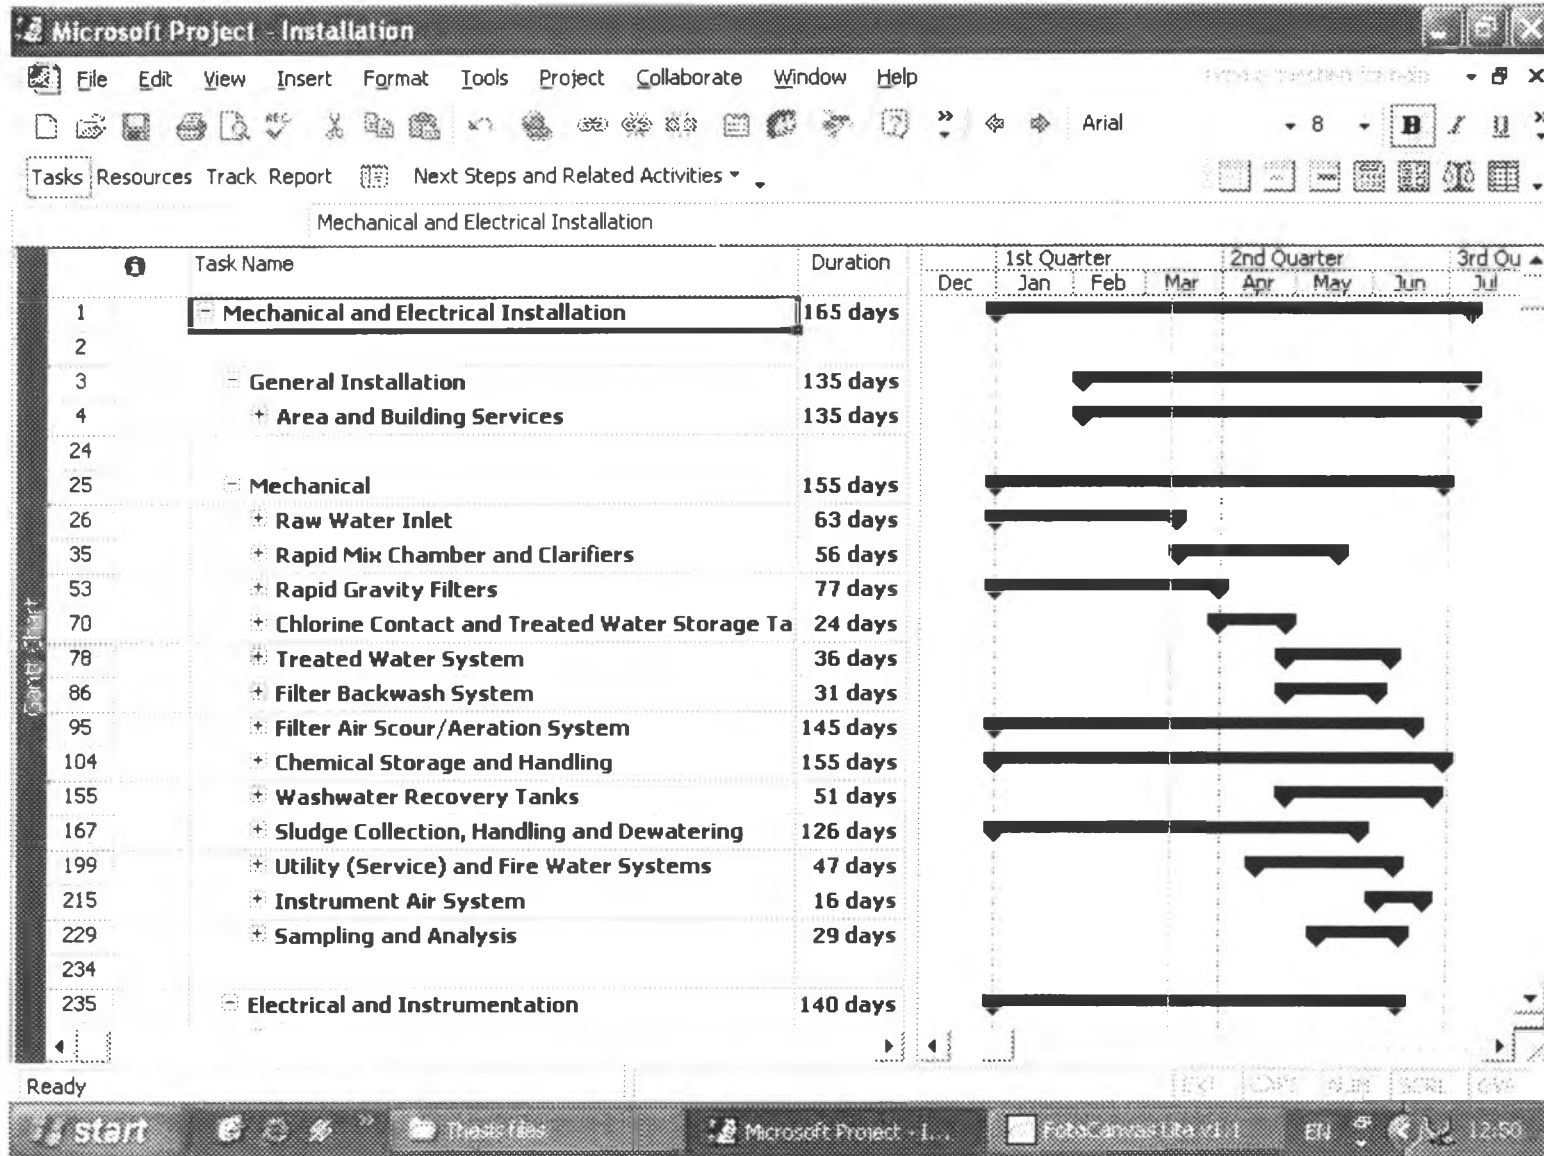

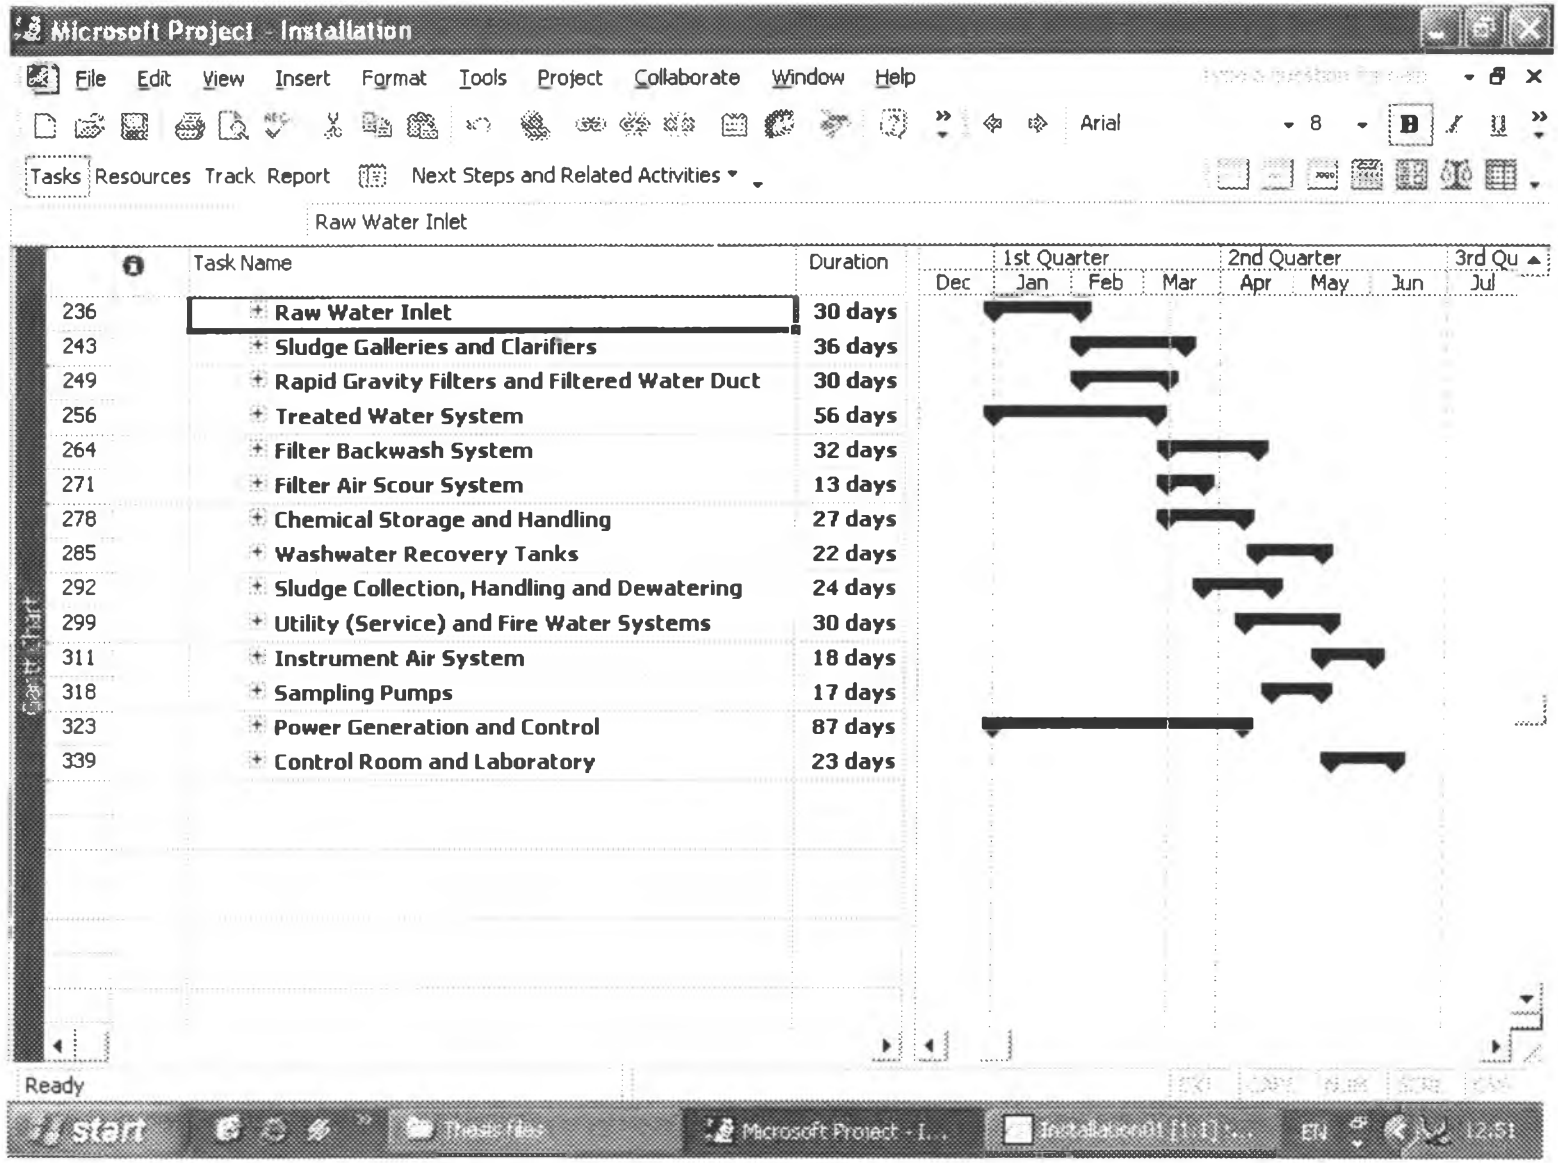

Biography

Tulyatep Uawithya was born on February 19th, 1979 in Bangkok, Thailand. He obtained his Bachelor Degree in Electrical Engineering from Tufts University in Medford, Massachusetts, USA. in 2002.

After he graduated, he started working for the case company as an Assistant Project Development Manager. Later in the year 2002, he had decided to continue his study for Master Degree in Engineering Management at the Regional Center for Manufacturing Systems Engineering, Faculty of Engineering, Chulalongkorn University, Thailand and University of Warwick, United Kingdom.



เลขที่ ๓๐๕

กระทรวงศึกษาธิการ
ประกาศนียบัตรฉบับนี้ให้ไว้เพื่อแสดงว่า

นายพัฒนชกร ผดุงชาติ

เกิดวันที่ ๒๕ เดือน พฤศจิกายน พ.ศ. ๒๕๒๘

สำเร็จการศึกษาตามหลักสูตร

มัธยมศึกษาตอนปลาย

จาก โรงเรียน โยธินบูรณะ

สังกัด สำนักงานคณะกรรมการการศึกษาขั้นพื้นฐาน จังหวัด กรุงเทพมหานคร

เมื่อวันที่ ๓๑ เดือน มีนาคม พุทธศักราช ๒๕๕๗

ขอให้ความสุขสวัสดิ์เจริญเทอญ

เจ้าพนักงานทะเบียน

